


NOTES:

1. All signs and cones to be in accordance with Chapter 8-2009, the TSRGD and current IAN's.
2. Works access and egress are indicative, exact locations to be agreed on site.
3. Safety zones are to be installed as required.
4. All signs to be located so as not to obscure signs or objects and should be ballasted near to ground level using sand filled hessian bags or sign straps.
5. All sign positions are indicative only and must be accurately positioned on site with good visibility and be clear of and obstructions or vegetation at all times.
6. Drawing not to scale
7. TM will comply with the Safety at Street Works and Road Works Code of Practice

Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	
Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	
Qty: 1 Ref: 2702 Start of temporary diversion route	
Qty: 2 Ref: 2702 Start of temporary diversion route	
Qty: 2 Ref: 2702 End of temporary diversion route	
Qty: 1 Ref: 2702 Start of temporary diversion route	
Qty: 2 Ref: 2703 Direction of temporary diversion route from junction ahead	
Qty: 2 Ref: 2703 Direction of temporary diversion route from junction ahead	
Qty: 2 Ref: 2704 Direction of temporary diversion route	
Qty: 2 Ref: 2704 Direction of temporary diversion route	
Qty: 4 Ref: 573 Direction to hazard left	
Qty: 4 Ref: 573 Direction to hazard right	
Qty: 2 Ref: 612 No left turn	
Qty: 2 Ref: 613 No right turn	
Qty: 6 Ref: 7001 Road works ahead	
Qty: 2 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Ahead Closed	
Qty: 2 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Closed	
Qty: 4 Ref: 7010-1 Nature of temporary hazard ahead - Road Ahead Closed	

Road Widths:

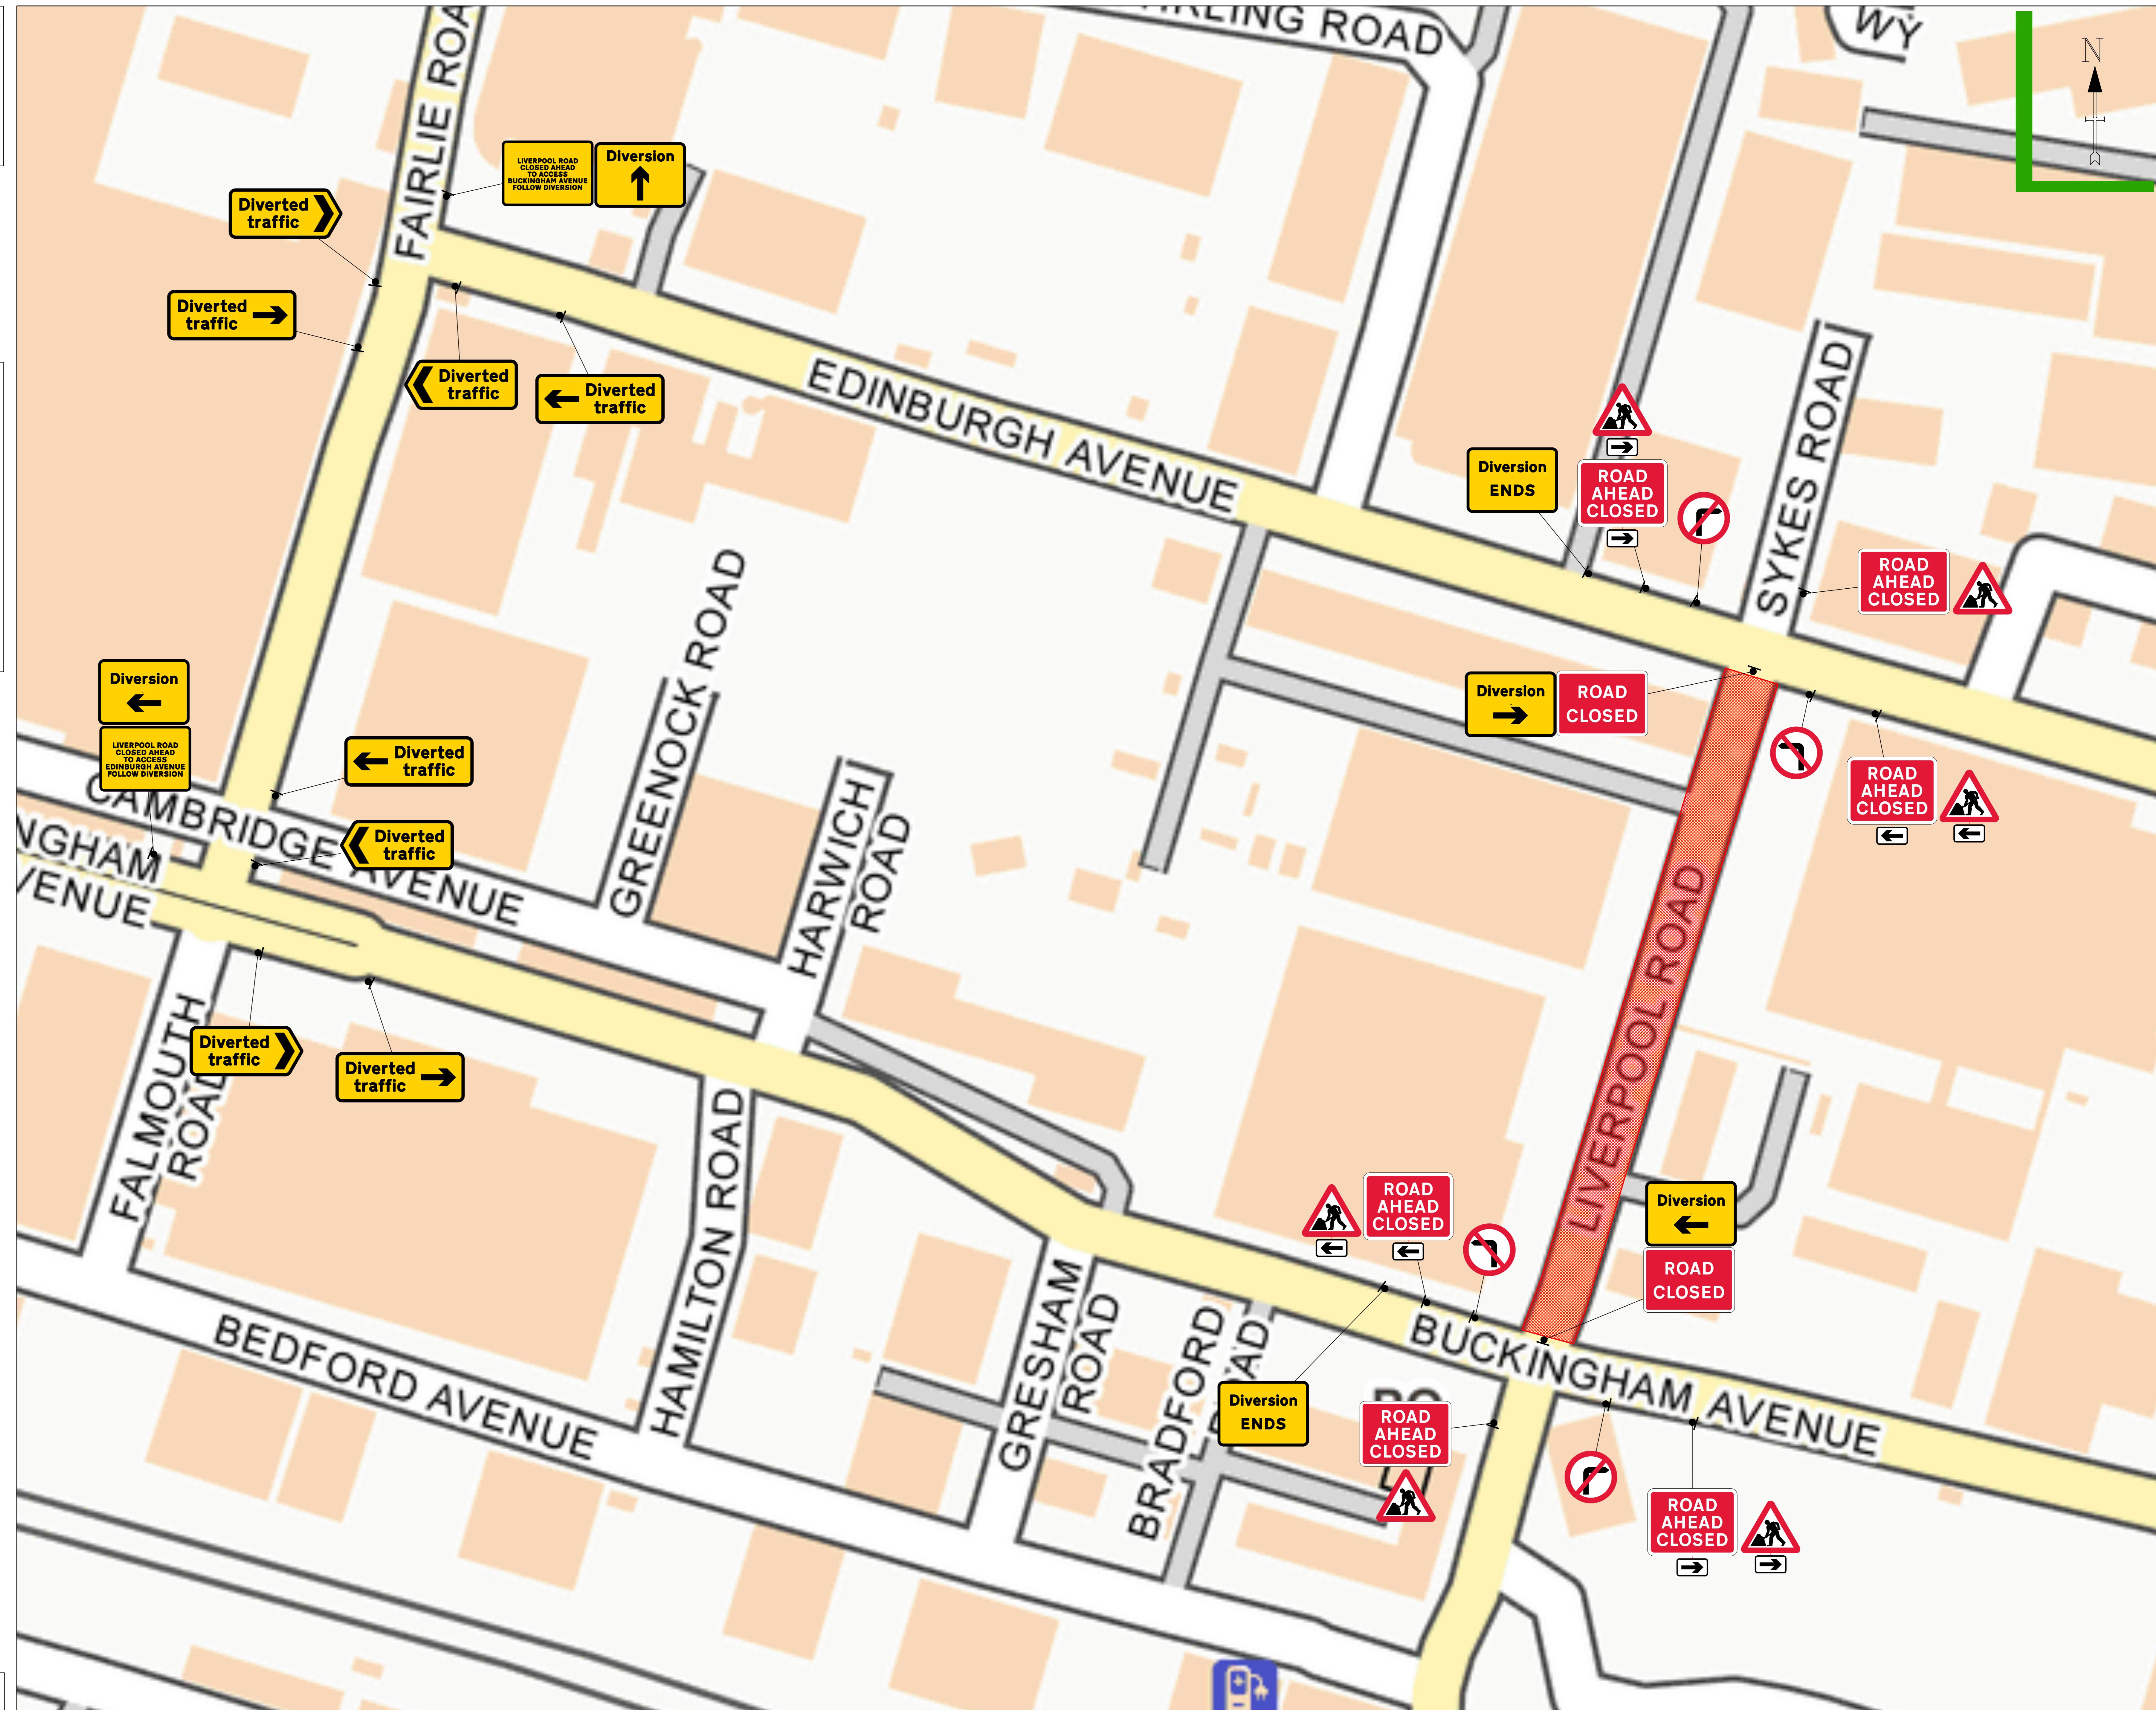

KEY:	SAFETY ZONE	CONE	Bus stop suspension
WORK AREA	• • •	PED BARRIER	Parking Bay suspension
SPOIL AREA	▲	NO PARKING CONE	

DETAILS OF THE ROAD	
	Liverpool Road
Drawn By	M Oprescu
Checked By	M Turcanu
Survey By	Client
Date Drawn	22/01/2026
Drawing No	IMGA232115
